Tri-Cities Remodeling Company
Printed: Nov 11, 2026
328 E Elk Ave Ste 2a, Elizabethton, TN 37643-3351
Phone: 423-512-1993
tricitiesremodelingco.com
TN License # 80259

Daily Logs List

Oct 19, 2026

Job: 1952 Sink Valley Road - Exterior and Coordination
Title:
Added By: Jesse Goodpaster
Log Notes:
Continued running decking
Ran decking on stair landing
Set stringers and treads
Attachments: 9











Oct 19, 2026

Job: 212 Collingwood Drive - Bathroom
Title:
Added By: Kevin Graham
Log Notes:
What was completed today?
Installed glass door
Applied first layer of mud

Next steps?
Sand
grout corners

Attachments: 5







Oct 19, 2026

Job: 212 Collingwood Drive - Bathroom
Title:
Added By: Jordan White
Log Notes:
What was completed today?
-Installed drywall
-started drywall finishing
-installed shower door

Next steps?
-finish drywall
-prime walls
-paint walls

Attachments: 21























Oct 19, 2026

Job: 25 Carson Ln - Kitchen
Title:
Added By: Nick Bennett
Log Notes:
What was completed today? Remaining final coat applied to corners. Touched up floor leveler. Laid LVP flooring. Put down protection over finished floor.
Next steps?

Attachments: 7









Oct 19, 2026

Job: 366 Gransley Ct - Basement Remodel
Title:
Added By: Jesse Jarman
Log Notes:
Marked location of all boxes, installed what boxes we had (underestimated how many boxes would be needed), ran 12/2 wire to almost all boxes, installed panel in its intended location, marked drywall on ceiling where to cut for home runs and SER path, cleaned up trash and debris

Attachments: 140






















































AX












































AX










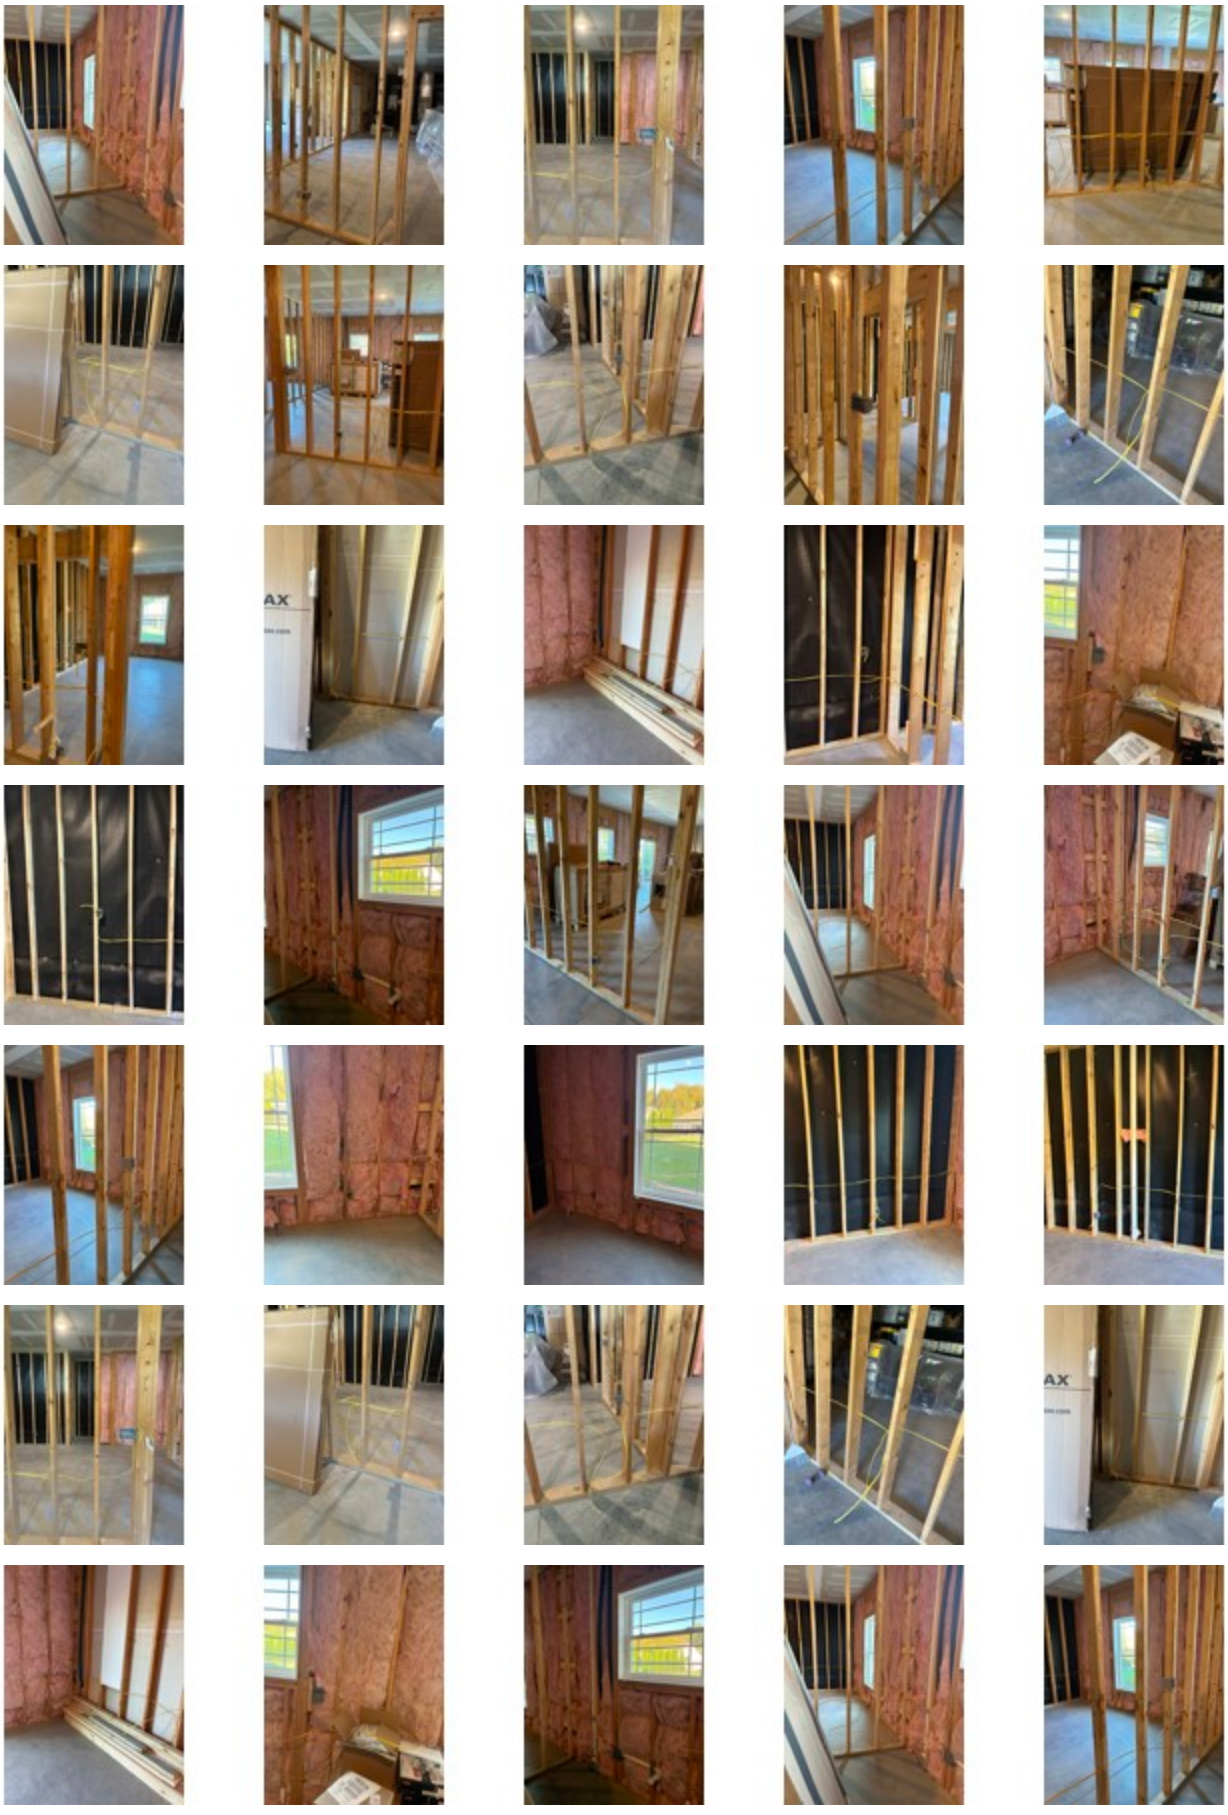

Oct 19, 2026

Job: 513 Chadwell Road - Rebuild

Title:
Added By: Kelvin Bradley
Log Notes:
What was completed today?samded all of downstairs and primes most of it

Next steps?
Attachments: 4






Oct 19, 2026

Job: 513 Chadwell Road - Rebuild
Title:
Added By: Caleb McCarty
Log Notes:
What was completed today?

Sanded all the drywall downstairs primed a lot of it

Next steps?
Attachments: 10












Oct 19, 2026

Job: 114 Whitaker Drive - Covered Deck
Title: Shane’s
Added By: Shane Quigley
Log Notes:
Extra material were picked up

Fred came by and addressed gutters leaking

Straighten joist
Cut off old screws that were protruding

Fixed vinyl siding
Attachments: 5







Oct 19, 2026

Job: 164 Kaluna Avenue - Covered Patio
Title: Shane's
Added By: Shane Quigley
Log Notes:
Guys framing roof, they will be adding sheathing and waterproofing

Called in for framing inspection, should happen tomorrow
Attachments: 5







Oct 19, 2026

Job: 205 Pawnee Street - Deck Building
Title: Shane's
Added By: Shane Quigley
Log Notes:
Concrete sidewalks poured over the weekend

Laundry room sink is being connected

Final grade completed

Spoke with Sarah, she wants mortar on fireplace stone where you can see mesh. That will be done this week.

Zack will take other mantle back to office, so Jeff M. can return it.

We will remove left over garbage

Spoke with Jeff S. he will pick up metal break today

Attachments: 12














Oct 19, 2026

Job: 25 Carson Ln - Kitchen
Title:
Added By: Justin Askew
Log Notes:
What was completed today?

-Skim coated all angles
-Sanded areas on walls and ceilings that were ready
-Installed flooring and laid floor protection

Next steps?
Attachments: 7









Oct 19, 2026

Job: 164 Kaluna Avenue - Covered Patio
Title:
Added By: Fred Nawrocki
Log Notes:
installed barge rafters and sub facia. installation of center and vent bay blocking
Attachments: 0

Oct 19, 2026

Job: 114 Whitaker Drive - Covered Deck
Title:
Added By: Fred Nawrocki
Log Notes:
went to reseal gutters and investigated leaks. wet gutters prevented sealant. due to seal tomorrow
Attachments: 0

Oct 19, 2026

Job: *Trucks
Title:
Added By: Zach Arnold
Log Notes:
What was completed today?

Next steps?
Weather Conditions:
Sunny Mon, Oct 19, 2026, 5:56 PM

72°F
35°F

Wind: 5 mph
Humidity: 90%
Total Precip: 0"

Attachments: 6








Oct 19, 2026

Job: 6 Wentworth Court - Kitchen

Title:
Added By: Chris Phillips
Log Notes:
What was completed today?

Next steps? drilled and installed cabinet knobs
Attachments: 3





Oct 19, 2026

Job: 112 Lands End Ct - Foundation
Title:
Added By: Chris Phillips
Log Notes:
What was completed today?

Next steps? drill 5/8 thick hole 10 in into the foundation left and right side of the cracks and then inserted a polyurethane resin to locate the water source and follow it back and stop it.
Attachments: 2




Oct 19, 2026

Job: 366 Gransley Ct - Basement Remodel
Title:
Added By: Warren Parsons
Log Notes:
picked up materials
installed boxes for outlets and switches
started pulling wire

Attachments: 22
























Oct 19, 2026

Job: 1952 Sink Valley Road - Exterior and Coordination
Title:
Added By: Joshua Ray
Log Notes:
completed decking on upper deck set 2nd stringer to landing and started treads

Attachments: 5







Oct 19, 2026

Job: 1952 Sink Valley Road - Exterior and Coordination
Title:
Added By: Quincy Killen
Log Notes:
What was completed today?
installed stringers going to landing to the second story of deck
continued installing deck boards
Attachments: 3





Oct 19, 2026

Job: Springfield Ln 130 - Addition
Title:
Added By: Santiago Rodriguez
Log Notes:
Painted on the waterproofing primer and installed the waterproof membrane 2 rows on 2 sides. cleaned up trash around the property.
Attachments: 8










Oct 19, 2026

Job: Springfield Ln 130 - Addition
Title:
Added By: Aaron Crawford
Log Notes:
Foundation work
Attachments: 2




Oct 19, 2026

Job: 164 Kaluna Avenue - Covered Patio
Title:
Added By: Peter Maley
Log Notes:
What was completed today?

Blocked front of rafter bays
mid span rafter blocking
barge rafters installed
sub fascia on front
sheathed roof (except for top row)
Attachments: 3





Oct 19, 2026

Job: 6 Wentworth Court - Kitchen
Title:
Added By: Steven Metcalf
Log Notes:
What was completed today?

go over remaining punch list items

Next steps?

Attachments: 5







Oct 19, 2026

Job: 366 Gransley Ct - Basement Remodel
Title:
Added By: Steven Metcalf
Log Notes:
What was completed today?
site visit to review framing, check on start of electrical, and meet with homeowners about location of bathroom door.

Next steps?
Attachments: 3





Oct 19, 2026

Job: 205 Pawnee Street - Deck Building
Title:
Added By: Zach Arnold
Log Notes:
What was completed today?
finish grade
Next steps?
Attachments: 5







Oct 19, 2026

Job: 4056 Black Oak Drive - Deck Building
Title:
Added By: Steven Metcalf
Log Notes:

What was completed today?

check on deck framing progress.

Next steps?

Attachments: 4






Oct 19, 2026

Job: 212 Collingwood Drive - Bathroom
Title:
Added By: Steven Metcalf
Log Notes:
What was completed today?
check on job progress and discuss projected finish date with Kevin.

Next steps?

Attachments: 4






Oct 19, 2026

Job: 205 Pawnee Street - Deck Building
Title:
Added By: Warren Parsons
Log Notes:
installed laundry room sink water lines and drain
verified no leaks

Attachments: 1



Oct 19, 2026

Job: *Trucks
Title:
Added By: Zach Arnold
Log Notes:
What was completed today?

Next steps?
Weather Conditions:
Sunny Mon, Oct 19, 2026, 8:25 AM

73°F
35°F
Wind: 4 mph
Humidity: 91%
Total Precip: 0"

Attachments: 4

